

**Citizens' Oversight Committee  
Project Tour  
Wednesday, 4/17/2019**


**Itinerary:**

- 8:45-9:00 Members arrive and board the van.
- 9:05 Van leaves D.O. and heads to Hillsdale.
- 9:20 Arrive at Hillsdale; Group tours new modular classroom building.
- 9:50 Depart Hillsdale and head to Anza.
- 10:00 Arrive at Anza; Group tours current construction site.
- 10:30 Depart Anza and head to Johnson.
- 10:50 Arrive at Johnson; Group tours future construction site.
- 11:20 Depart Johnson and head to D.O.
- 11:30 Arrive back at D.O.; Tour concludes.





# Anza Elementary School

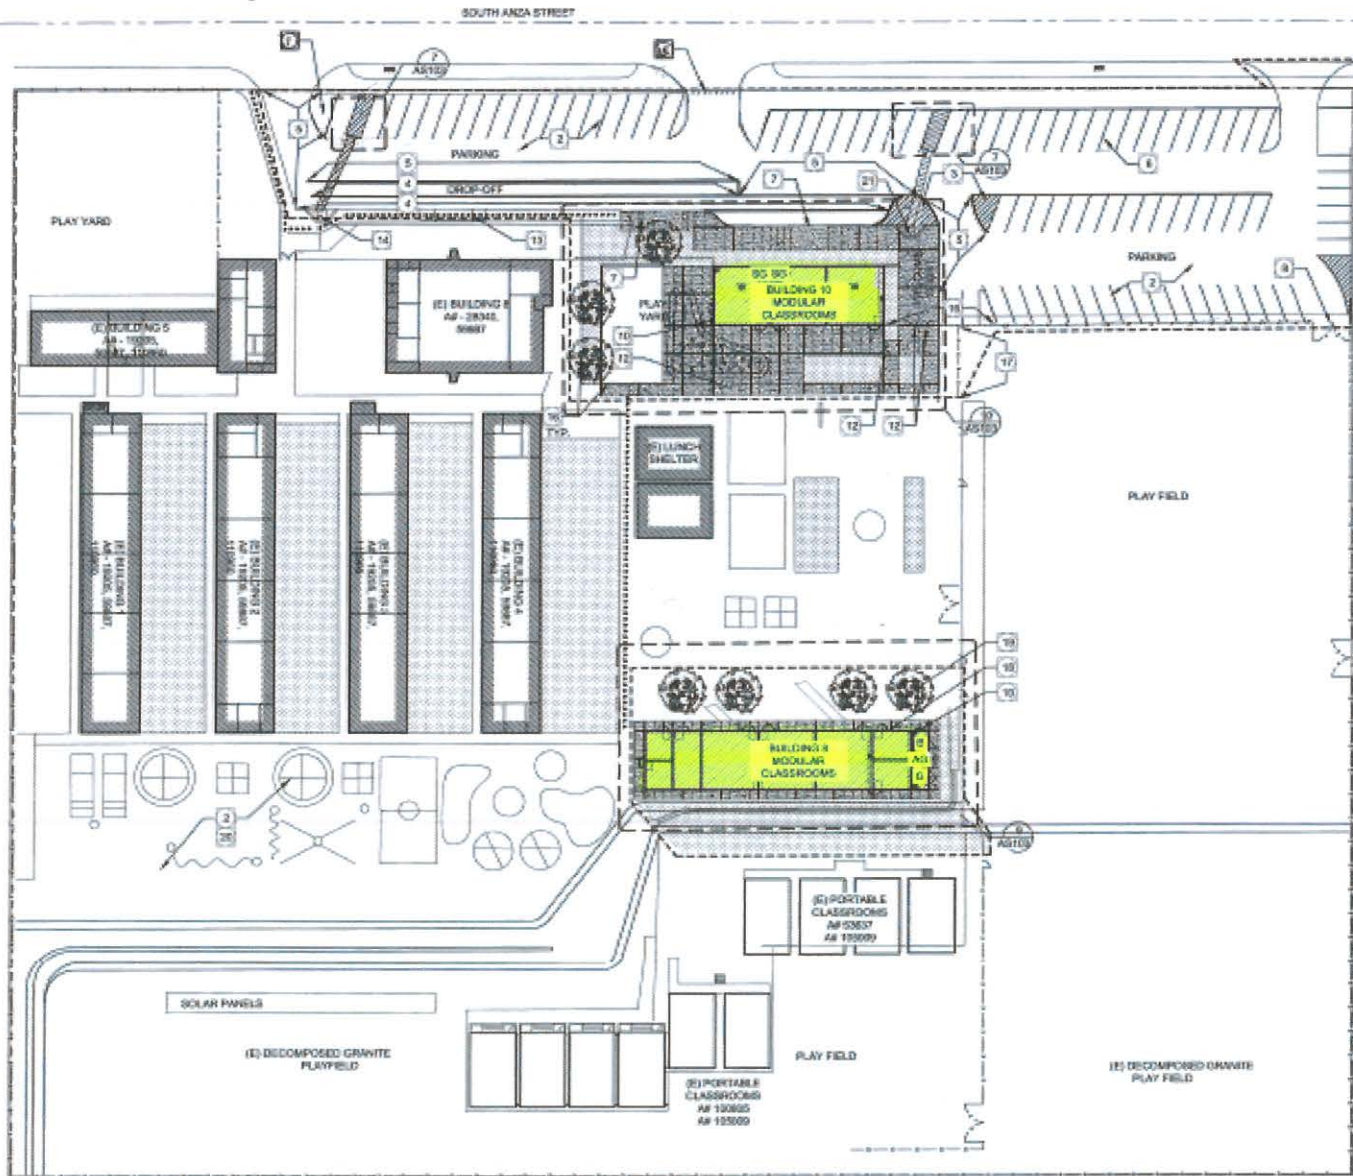

### Scope of Work (Phase 1):

**Demolition/removal:** 5 portable classroom buildings.

**Addition:** 2 new modular classroom buildings, including: 6 classrooms; 5 small group/office spaces; student and staff restrooms. Landscaping and new preschool playground.


**Renovation:** Parking lot improvements.

Architect: HED

**Contractor:** Conan Construction

**Construction Start Date:**  
4/1/2019

**Estimated Construction Completion Date: 8/9/2019**

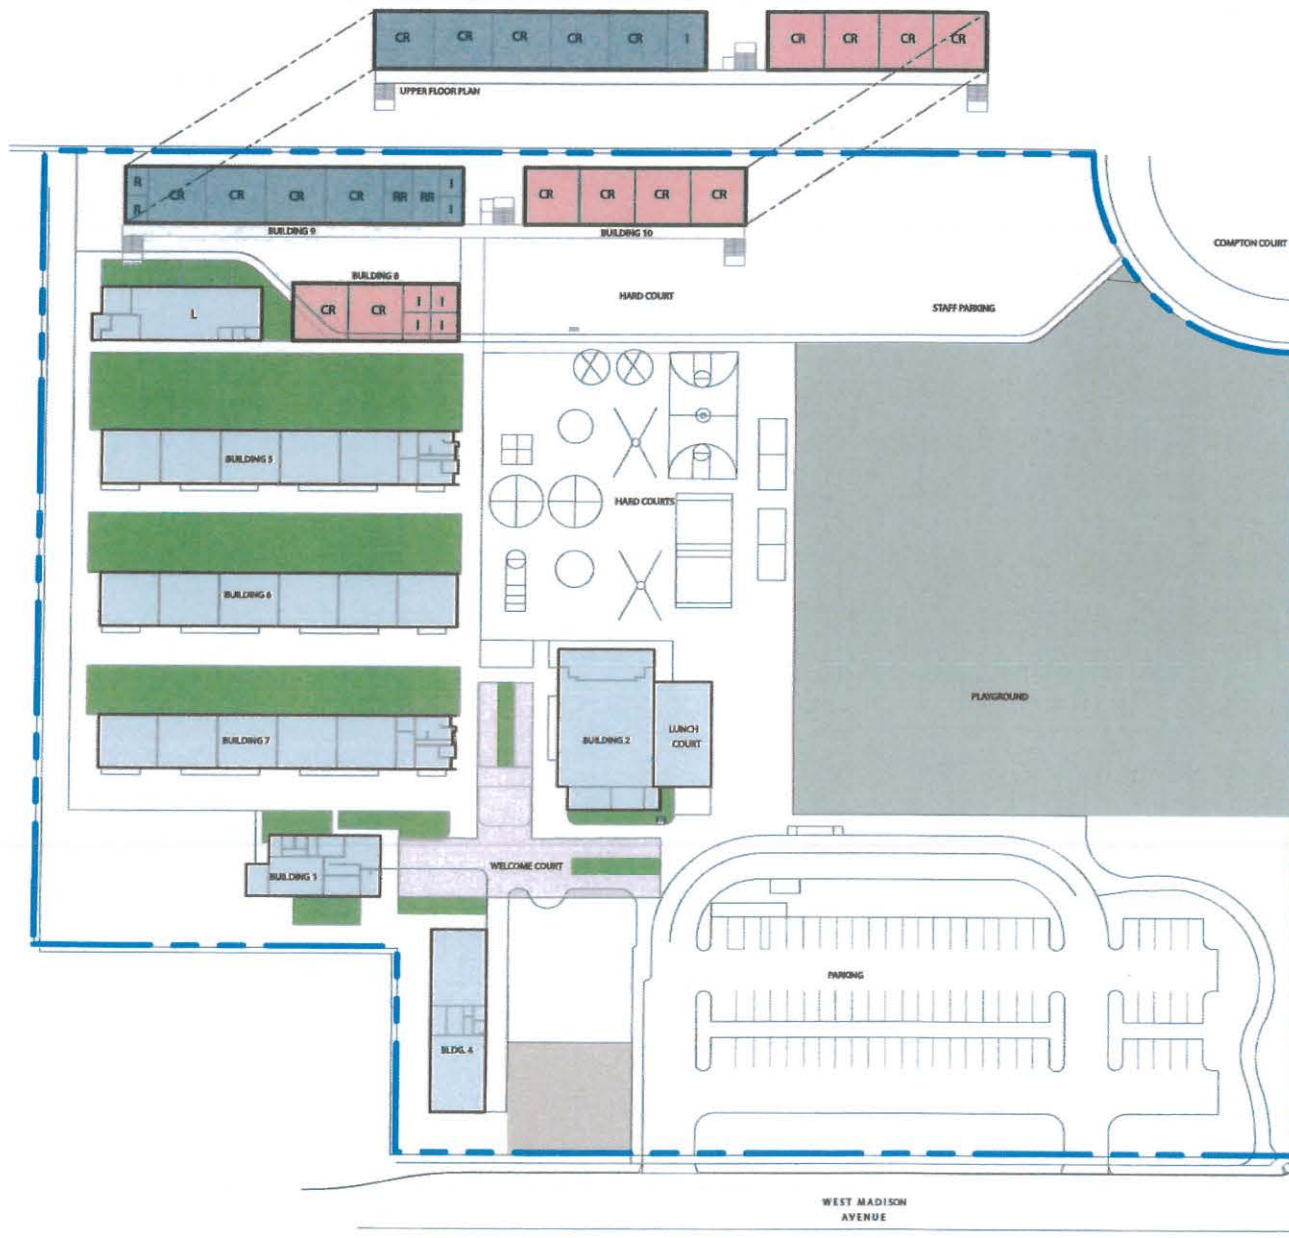

LEGEND:

R STAFF RESTROOM  
 RR STUDENT RESTROOM  
 CR CLASSROOM  
 I ITINERANT SPACE

EXISTING  
 PROPOSED MODULAR BUILDING PHASE 1  
 PROPOSED MODULAR BUILDING PHASE 2

TOTAL: 19 CLASSROOMS AT 30' X 32'  
 7 ITINERANT SPACES



HED

225 Broadway, Suite 1300  
 San Diego, California 92101  
 (619) 398-3800  
 www.hed.design

Copyright © 2018

JOHNSON ELEMENTARY SCHOOL  
 CLASSROOM REPLACEMENT

Cajon Valley Union School District

Title: Preliminary Site Plan  
 Date: 10/09/2018  
 Scale: 1"=100'-0"  
 Sketch No.: JES-SP-3



[illegible]

**Estimated Construction Completion Date:** Summer 2020
